

Project to Enhance Learning Experience at Camp Greenough with Amateur Radio

March 6, 2023

Norm Cantin – President BARC

Status – March 6, 2023

- Storage room wall replaced Door relocated
- 3 of 4 walls framed
- Old wiring removed / relocated
- Florescent strip light relocated in line with existing door
- Door opening header insufficient Install LVL beam(s) to meet code
- Exterior door quotes / ordering in process
- Internet / Fiber infrastructure planning in process
- Poles scheduled to be installed 2nd week of March

Good Progress on Initial Room Construction

3 Walls Framed – Door Relocated




Men at Work



Special Thanks to Nick Bertazzoni & Mark Avery

Draft Room Layout – Work in Progress

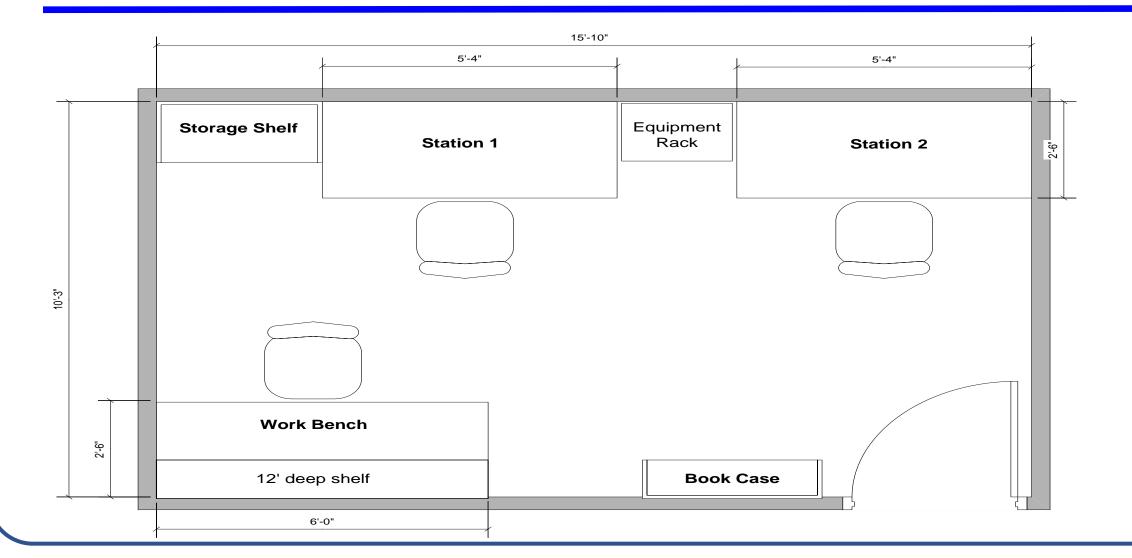

5

Donations Continue to Increase

- Building advise and oversite Evergreen Construction
- Framing lumber Shepley Wood
- Labor BARC
- Tree work Clear Cut Tree reduced rate
- Electrical wiring Avery Electric
- Telephone Poles Eversource
- Fiber cable and components Comcast

- Mini Splits Murphy's
- Blue Board Drywall Masonry
- Plastering Oceanside Plastering Company
- Paint Hubbert Paint
- Drop ceiling Mid Cape Home Center

ARRL Grant Significantly Supplemented by Local Donations

ARRL Grant Increased Substantially with Donation's from Local Businesses




Back-up

Status – Feb 6, 2023

- 15 trees cut down Clear Cut, Mark Avery
- Telephone pole locations marked
- Telephone pole installation over the next few weeks, weather depending – Eversource
- Basement cleanup complete
- Building permit received
- Electrical permit received

Ready to start framing the room

Basement Room Layout

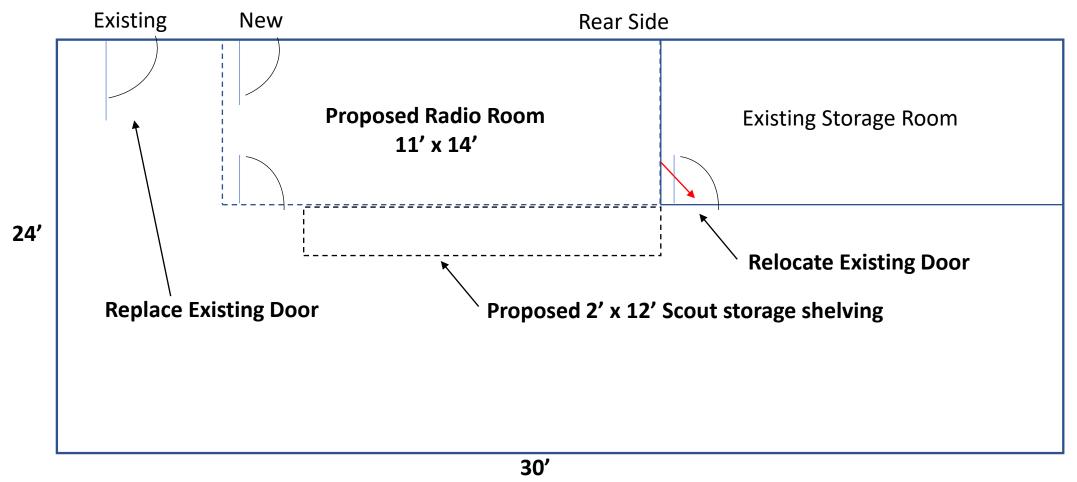

Antenna / Pole Locations



Radio Room Enhancement to Maushop Lodge



- Cleanup and organize basement

- Build and furnish 11' x 14' Radio Room

- Add exterior entrance to radio room
- Replace damaged existing door

Cleanup Complete – Ready to Frame Room



Thanks to Mark N1ZPO, Don KT1OK, Don K1DCA, Rob K1UI, Jim KC1IPU

15 Trees Removed



Big Boy Toys – Do Yeomans Work!



